
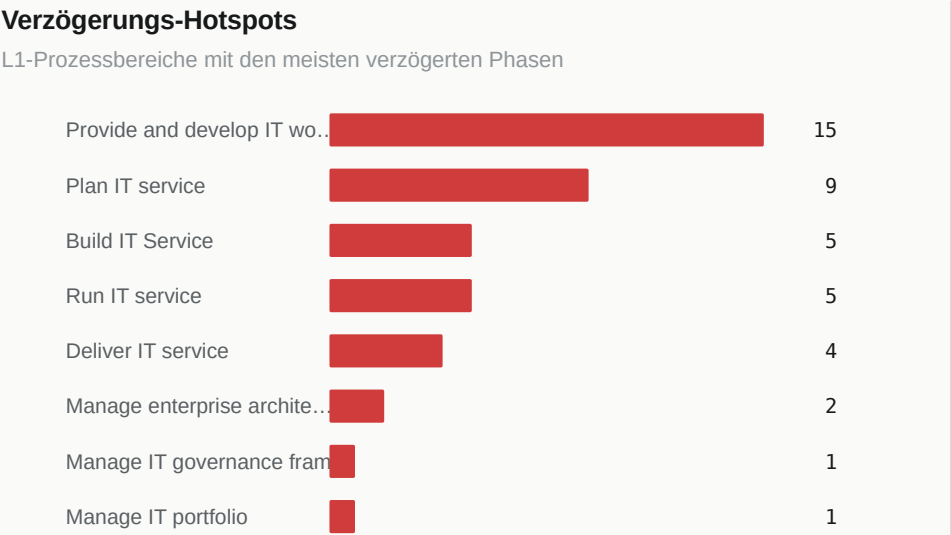
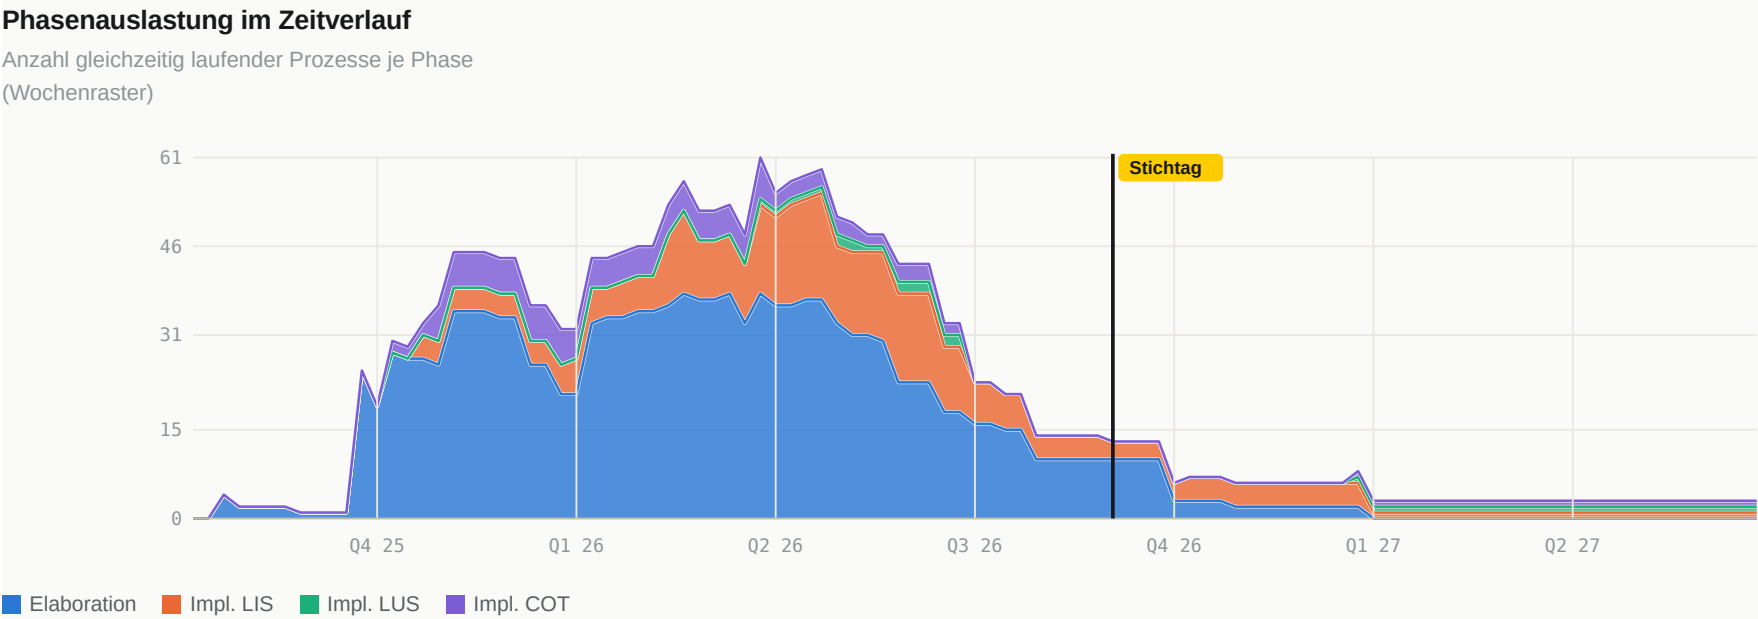


AUSWERTUNG


Portfolio-Überblick

124 von 124 Prozesse

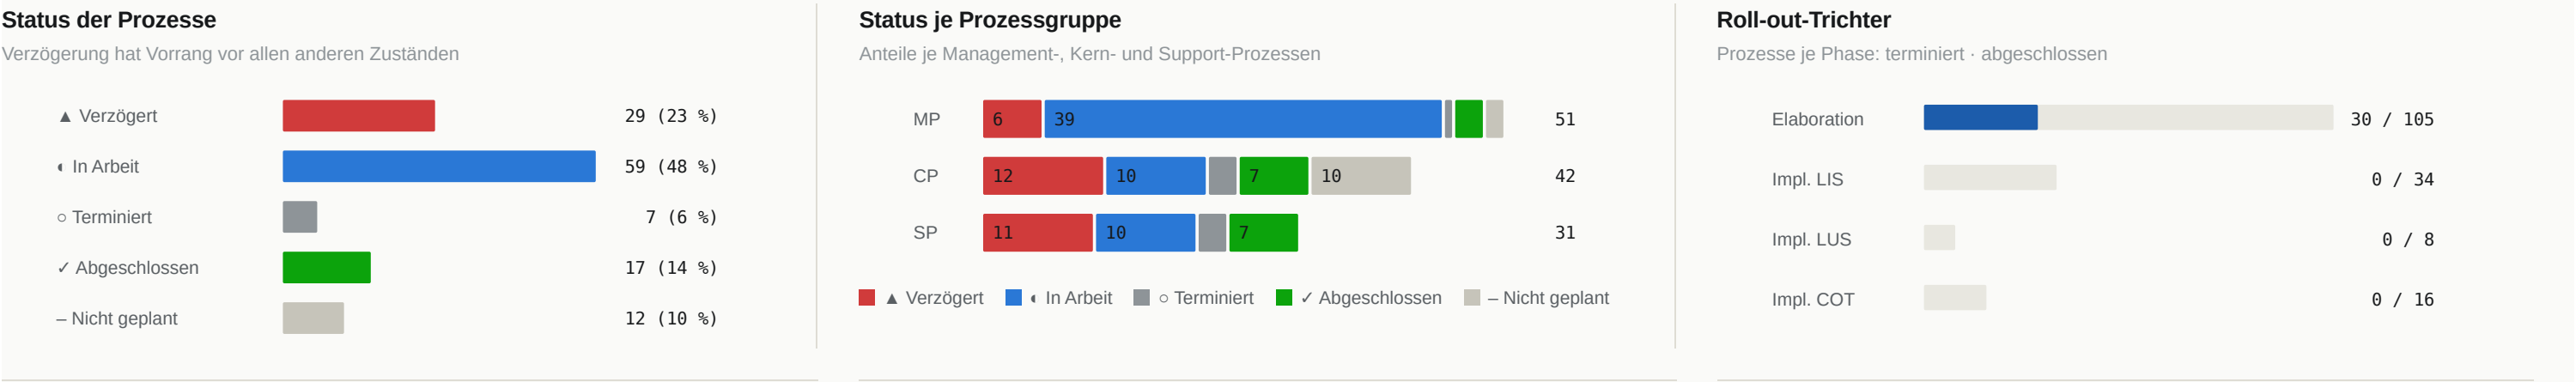


Fortschritt je Initiative

Ø Arbeitsfortschritt, Balkenbreite = Anzahl Prozesse

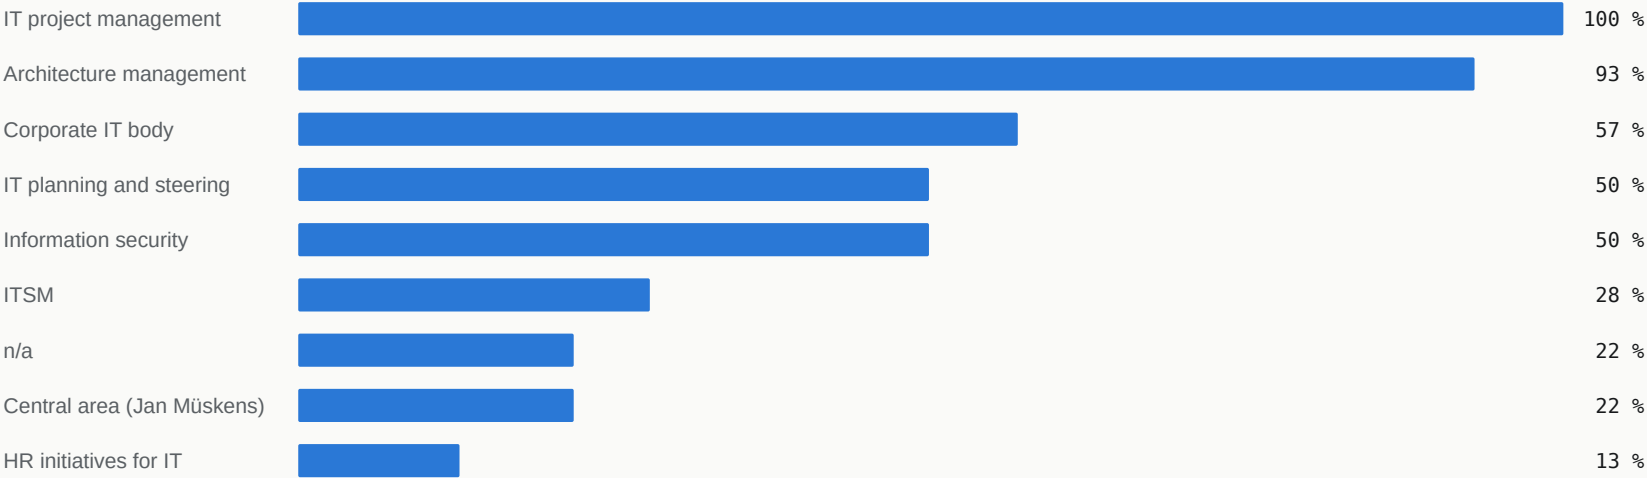

Portfolio je Process Manager

Verantwortungsumfang und Verzögerungsquote

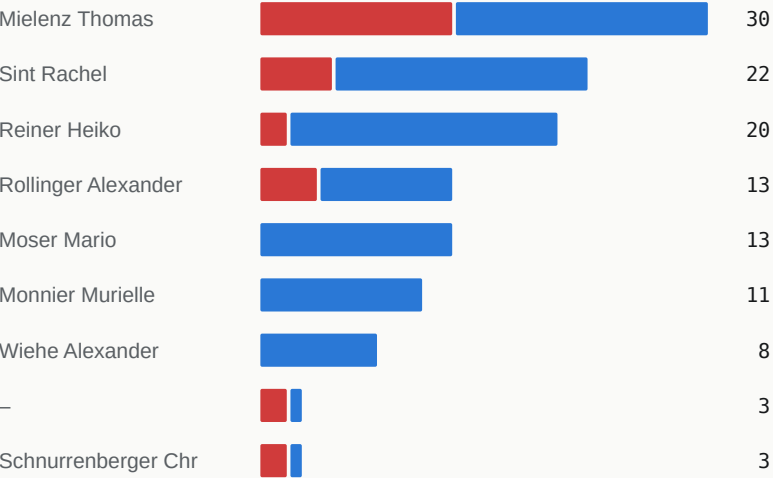

PLANUNG

Portfolio-Timeline

19 sichtbare Zeilen

PROZESS		% FERTIG	Q3 2025	Q4 2025	Q1 2026	Q2 2026	Q3 2026	Q4 2026	Q1 2027	Q2 2027	Q3 2027
	MP	Manage IT strategy	L1	50%							
	+ MP	Manage IT governance framework	L1	50%							
	+ MP	Manage enterprise architecture	L1	0%							
	+ MP	Manage IT portfolio	L1	78%							
	+ MP	Manage and control IT financials	L1	50%							
	MP	Manage IT stakeholder relationships	L1	0%							
	+ MP	Manage IT processes and continuo...	L1	21%							
	+ MP	Manage IT risks and compliance	L1	22%							
	+ CP	Plan IT service	L1	100%							
	+ CP	Build IT Service	L1	41%							
	+ CP	Deliver IT service	L1	0%							
	+ CP	Run IT service	L1	17%							
	+ SP	Ensure Information security	L1	50%							
	+ SP	Manage IT project	L1	100%							
	SP	Manage IT sourcing and procurement	L1	25%							
	+ SP	Provide and develop IT workforce	L1	15%							
	SP	Ensure performance and conforma...	L1	0%							
	SP	Manage IT knowledge	L1	100%							
	SP	Leverage IT innovation	L1	25%							

Elaboration Impl. LIS Impl. LUS Impl. COT Sammelbalken (Teilprozesse) verzögert Stichtag 01.09.2026

DATENBASIS

Detailtabelle

124 Prozesse sichtbar von 124

124 Zeilen															
PROZESS ▲	GRUPPE ⌵	EBENE ⌵	INITIATIVE ⌵	STATUS ⌵	% FERTIG ⌵	START ⌵	ENDE ⌵	DAUER (T) ⌵	ELABORATION ⌵	INITIATIVE LEAD ⌵	PROCESS MANAGER ⌵	CONSULTANT ⌵	FREIGABE ⌵	KOMMENTAR ⌵	
Analyse architecture impact Plan IT service › Evaluate and qualify IT demand › Analyse arc...	CP	L3	Corporate IT body	▲ Verzögert	100%	01.08.2025	30.04.2026	195	✓ Abgeschlossen	Pernet Benoit (LEC) (MIN)	Mielenz Thomas (LMT)	Kunz Christina (LIS-MHP)	–	–	
Analyse process Manage IT processes and continuous improvement › Perform ...	MP	L3	ITSM	✓ Abgeschlossen	100%	01.10.2025	01.10.2025	1	✓ Abgeschlossen	Rollinger Alexander (LIS)	Reiner Heiko (HAU-ITSA)	Hoermann Patrick (LLI)	18.09.2025	–	
Apply cost model to calculate service cost per unit Manage and control IT financials › Model and allocate IT costs ...	MP	L3	IT planning and steering	◀ In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–	
Approve and communicate budget plan Manage and control IT financials › Create and maintain IT bud...	MP	L3	IT planning and steering	◀ In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Mielenz Thomas (LMT)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–	
Approve IT demand Plan IT service › Approve IT demand	CP	L2	Corporate IT body	▲ Verzögert	100%	01.08.2025	31.03.2026	1	✓ Abgeschlossen	Spieth Tina (LIS)	Mielenz Thomas (LMT)	Kunz Christina (LIS-MHP)	19.08.2025	–	
Assign personnel resources to IT project Manage IT project › Assign personnel resources to IT project	SP	L2	IT project management	✓ Abgeschlossen	100%	14.07.2025	10.12.2025	1	✓ Abgeschlossen	Mühlbacher Christian (LIS)	Rollinger Alexander (LIS)	Frank Maren (LIS)	–	–	
Attract and hire employees Provide and develop IT workforce › Attract and hire employees	SP	L2	HR initiatives for IT	▲ Verzögert	18%	01.10.2025	31.12.2026	327	◀ In Arbeit	Kiesewetter Ivana (LIS)	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–	
Build IT Service Build IT Service	CP	L1	ITSM	◀ In Arbeit	41%	–	–	–	– Ohne Angabe	Dalek Martin (LIS)	Wiehe Alexander (COB)	Kunz Christina (LIS-MHP)	–	–	
Close IT project Manage IT project › Close IT project	SP	L2	IT project management	✓ Abgeschlossen	100%	14.07.2025	10.12.2025	1	✓ Abgeschlossen	Mühlbacher Christian (LIS)	Rollinger Alexander (LIS)	Frank Maren (LIS)	18.09.2025	–	
Collect and consolidate budget from stakeholders Manage and control IT financials › Create and maintain IT bud...	MP	L3	IT planning and steering	◀ In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Mielenz Thomas (LMT)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–	
Compare actual cost to budget forecast Manage and control IT financials › Manage IT costs › Compare...	MP	L3	IT planning and steering	◀ In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–	
Conduct market analysis and compile long or short list Build IT Service › Design IT service › Perform software selectio...	CP	L4	Architecture management	✓ Abgeschlossen	100%	01.10.2025	30.04.2026	1	✓ Abgeschlossen	Preiss Matthias (LBC)	Reiner Heiko (HAU-ITSA)	Hoermann Patrick (LLI)	14.10.2025	–	
Create and maintain IT budgets Manage and control IT financials › Create and maintain IT bud...	MP	L2	IT planning and steering	◀ In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Mielenz Thomas (LMT)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–	
Create, approve and publish trainings for IT workforce within IT Training Catalogue Provide and develop IT workforce › Perform, learn and grow › ...	SP	L3	HR initiatives for IT	◀ In Arbeit	50%	01.10.2025	30.04.2026	152	◀ In Arbeit	Grabmair Melanie (LIS)	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–	

PROZESS ▲	GRUPPE ⌵	EBENE ⌵	INITIATIVE ⌵	STATUS ⌵	% FERTIG ⌵	START ⌵	ENDE ⌵	DAUER (T) ⌵	ELABORATION ⌵	INITIATIVE LEAD ⌵	PROCESS MANAGER ⌵	CONSULTANT ⌵	FREIGABE ⌵	KOMMENTAR ⌵	
DC/DCC/MSD IT-compliance Manage IT risks and compliance › Manage IT compliance › DC...	MP	L3	Central area (Jan Müskens)	In Arbeit	25%	01.10.2025	30.09.2026	261	In Arbeit	Mueskens Jan (LHO)	Monnier Murielle (LEC)	Kreis Andreas (LLI)	–	–	
Define cost allocation principles Manage and control IT financials › Model and allocate IT costs ...	MP	L3	IT planning and steering	In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–	
Define financial management framework Manage and control IT financials › Manage finance and accoun...	MP	L3	IT planning and steering	In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–	
Define solution target architecture Build IT Service › Design IT service › Define solution target arc...	CP	L3	Architecture management	Verzögert	50%	14.01.2026	22.06.2026	114	In Arbeit	Hammer Marco (AER)	Nussbaumer Florian (LBC)	Hoermann Patrick (LLI)	–	–	
Deliver IT service Deliver IT service	CP	L1	ITSM	Terminiert	0%	01.04.2026	17.06.2026	56	– Ohne Angabe	–	Schnurrenberger Christoph (LIS-LIN)	–	–	–	
Deploy IT service Build IT Service › Deploy IT service	CP	L2	ITSM	In Arbeit	0%	04.05.2026	31.07.2026	–	In Arbeit	Dalek Martin (LIS)	Wiehe Alexander (COB)	Kunz Christina (LIS-MHP)	–	–	
Design IT service Build IT Service › Design IT service	CP	L2	ITSM	In Arbeit	50%	04.05.2026	31.07.2026	–	In Arbeit	Dalek Martin (LIS)	Wiehe Alexander (COB)	Kunz Christina (LIS-MHP)	–	–	
Develop and customise IT service Build IT Service › Develop and customise IT service	CP	L2	ITSM	In Arbeit	0%	04.05.2026	31.07.2026	–	In Arbeit	Dalek Martin (LIS)	Wiehe Alexander (COB)	Kunz Christina (LIS-MHP)	–	–	
Develop and maintain IT BPM framework Manage IT processes and continuous improvement › Develop ...	MP	L2	ITSM	Abgeschlossen	100%	04.08.2025	16.10.2025	1	Abgeschlossen	Rollinger Alexander (LIS)	Reiner Heiko (HAU-ITSA)	Hoermann Patrick (LLI)	18.09.2025	–	
Develop preliminary budget plan Manage and control IT financials › Create and maintain IT bud...	MP	L3	IT planning and steering	In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Mielenz Thomas (LMT)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–	
Elaborate to-be process Manage IT processes and continuous improvement › Perform ...	MP	L3	ITSM	In Arbeit	25%	12.01.2026	31.05.2026	100	In Arbeit	Rollinger Alexander (LIS)	Reiner Heiko (HAU-ITSA)	Rollinger Alexander (LIS)	18.09.2025	–	
Ensure Information security Ensure Information security	SP	L1	Information security	In Arbeit	50%	16.10.2025	16.10.2025	1	– Ohne Angabe	Da Silva Alessandro (LIN)	Monnier Murielle (LEC)	Rollinger Alexander (LIS)	–	–	
Ensure IT service continuity Run IT service › Ensure IT service continuity	CP	L2	ITSM	Nicht geplant	0%	–	–	–	– Ohne Angabe	–	Sint Rachel (LBH)	Schroeder Michael (LIS), Boehme Matthias (LIS-BPMO)	–	–	
Ensure performance and conformance of IT services Ensure performance and conformance of IT services	SP	L1	ITSM	Verzögert	0%	–	–	–	Verzögert	–	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	–	
Establish cost allocation model Manage and control IT financials › Model and allocate IT costs ...	MP	L3	IT planning and steering	In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–	

PROZESS ▲	GRUPPE ⌵	EBENE ⌵	INITIATIVE ⌵	STATUS ⌵	% FERTIG ⌵	START ⌵	ENDE ⌵	DAUER (T) ⌵	ELABORATION ⌵	INITIATIVE LEAD ⌵	PROCESS MANAGER ⌵	CONSULTANT ⌵	FREIGABE ⌵	KOMMENTAR ⌵
Establish financial accounting structure Manage and control IT financials › Manage finance and account...	MP	L3	IT planning and steering	In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–
Evaluate and qualify IT demand Plan IT service › Evaluate and qualify IT demand	CP	L2	Corporate IT body	Verzögert	100%	01.08.2025	30.04.2026	195	✓ Abgeschlossen	Spieth Tina (LIS)	Mielenz Thomas (LMT)	Kunz Christina (LIS-MHP)	10.12.2025	–
Evaluate success of IT service rollout Build IT Service › Evaluate success of IT service rollout	CP	L2	ITSM	In Arbeit	0%	04.05.2026	31.07.2026	–	In Arbeit	Dalek Martin (LIS)	Wiehe Alexander (COB)	Kunz Christina (LIS-MHP)	–	–
Gather relevant cost and consumption data Manage and control IT financials › Model and allocate IT costs ...	MP	L3	IT planning and steering	In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–
Handle IT Incident Run IT service › Provide IT service support › Handle IT Incident	CP	L3	ITSM	In Arbeit	75%	13.01.2026	19.03.2026	48	In Arbeit	Kuerschner Philipp (LIS)	Sint Rachel (LBH)	Schroeder Michael (LIS)	19.03.2026	–
Handle IT problem Run IT service › Provide IT service support › Handle IT problem	CP	L3	ITSM	In Arbeit	75%	13.01.2026	19.03.2026	48	In Arbeit	Kuerschner Philipp (LIS)	Sint Rachel (LBH)	Schroeder Michael (LIS)	19.03.2026	–
Handle IT service order Deliver IT service › Handle IT service order	CP	L2	ITSM	Verzögert	0%	01.04.2026	17.06.2026	56	Verzögert	–	Schnurrenberger Christoph (LIS-LIN)	–	–	–
Handle IT service request Run IT service › Provide IT service support › Handle IT service ...	CP	L3	ITSM	Abgeschlossen	100%	02.02.2026	19.03.2026	–	✓ Abgeschlossen	Kuerschner Philipp (LIS)	Sint Rachel (LBH)	Frank Maren (LIS)	–	–
Identify process and determine goals Manage IT processes and continuous improvement › Perform ...	MP	L3	ITSM	In Arbeit	25%	12.01.2026	31.05.2026	100	In Arbeit	Rollinger Alexander (LIS)	Reiner Heiko (HAU-ITSA)	Rollinger Alexander (LIS)	18.09.2025	–
Implement and maintain IT job architecture Provide and develop IT workforce › Manage HR4IT strategy, g...	SP	L3	HR initiatives for IT	Verzögert	0%	16.10.2025	31.05.2026	162	Verzögert	Amelang Nicole (LIS)	Rollinger Alexander (LIS)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Implement cost allocation to stakeholders or companies Manage and control IT financials › Model and allocate IT costs ...	MP	L3	IT planning and steering	In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–
Implement process Manage IT processes and continuous improvement › Perform ...	MP	L3	ITSM	In Arbeit	25%	12.01.2026	31.05.2026	100	In Arbeit	Rollinger Alexander (LIS)	Reiner Heiko (HAU-ITSA)	Rollinger Alexander (LIS)	19.09.2025	–
Implement to improve Manage IT risks and compliance › Manage IT compliance › Im...	MP	L3	Central area (Jan Müskens)	In Arbeit	25%	01.10.2025	30.09.2026	261	In Arbeit	Mueskens Jan (LHO)	Monnier Murielle (LEC)	–	–	–
Initiate corrective or preventive actions Manage and control IT financials › Manage IT costs › Initiate co...	MP	L3	IT planning and steering	In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–
Initiate IT project Manage IT project › Initiate IT project	SP	L2	IT project management	Abgeschlossen	100%	14.07.2025	10.12.2025	1	✓ Abgeschlossen	Mühlbacher Christian (LIS)	Rollinger Alexander (LIS)	Frank Maren (LIS)	18.09.2025	–
Leverage IT innovation Leverage IT innovation	SP	L1	ITSM	In Arbeit	25%	01.05.2026	31.10.2026	55	– Ohne Angabe	Abbondio Viviana (LIS)	Sint Rachel (LBH)	Chen Leilei (LIS-BPMO)	–	–

PROZESS ▲	GRUPPE ⌵	EBENE ⌵	INITIATIVE ⌵	STATUS ⌵	% FERTIG ⌵	START ⌵	ENDE ⌵	DAUER (T) ⌵	ELABORATION ⌵	INITIATIVE LEAD ⌵	PROCESS MANAGER ⌵	CONSULTANT ⌵	FREIGABE ⌵	KOMMENTAR ⌵
Maintain CMDB Run IT service › Operate and maintain IT service › Maintain C...	CP	L3	ITSM	◀ In Arbeit	50%	14.01.2026	16.06.2026	91	◀ In Arbeit	Kretz Lucas (COC-COT-IT)	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	–
Maintain IT asset database Run IT service › Operate and maintain IT service › Maintain IT ...	CP	L3	ITSM	– Nicht geplant	0%	–	–	–	– Ohne Angabe	–	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	–
Maintain IT glossary Manage IT governance framework › Maintain IT glossary	MP	L2	Corporate IT body	▲ Verzögert	25%	07.01.2026	17.01.2026	8	– Ohne Angabe	Felder Max (LLI)	Mielenz Thomas (LMT)	Kunz Christina (LIS-MHP)	–	–
Maintain standard change catalogue for IT service Run IT service › Operate and maintain IT service › Maintain sta...	CP	L3	ITSM	– Nicht geplant	0%	–	–	–	– Ohne Angabe	–	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	–
Maintan and adjust budget Manage and control IT financials › Create and maintain IT bud...	MP	L3	IT planning and steering	◀ In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Mielenz Thomas (LMT)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–
Manage a common approach to contiual improvement Manage IT processes and continuous improvement › Manage ...	MP	L3	ITSM	– Nicht geplant	0%	–	16.10.2025	–	– Ohne Angabe	Kuerschner Philipp (LIS)	Reiner Heiko (HAU-ITSA)	Boehme Matthias (LIS-BPMO), Rollinger Alexander (LIS)	–	–
Manage and control IT financials Manage and control IT financials	MP	L1	IT planning and steering	◀ In Arbeit	50%	15.10.2025	31.07.2026	208	◀ In Arbeit	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–
Manage continual improvement initiative Manage IT processes and continuous improvement › Manage ...	MP	L3	ITSM	– Nicht geplant	0%	–	16.10.2025	–	– Ohne Angabe	Kuerschner Philipp (LIS)	Reiner Heiko (HAU-ITSA)	Boehme Matthias (LIS-BPMO), Rollinger Alexander (LIS)	–	–
Manage continuous improvement Manage IT processes and continuous improvement › Manage ...	MP	L2	ITSM	▲ Verzögert	0%	01.10.2025	30.01.2026	88	▲ Verzögert	Kuerschner Philipp (LIS)	Reiner Heiko (HAU-ITSA)	Boehme Matthias (LIS-BPMO), Rollinger Alexander (LIS)	–	–
Manage enterprise architecture Manage enterprise architecture	MP	L1	Corporate IT body	▲ Verzögert	0%	16.10.2025	16.07.2026	195,85	▲ Verzögert	–	–	–	–	–
Manage finance and accounting Manage and control IT financials › Manage finance and accoun...	MP	L2	IT planning and steering	◀ In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Mielenz Thomas (LMT)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–
Manage HR4IT service demand Provide and develop IT workforce › Manage HR4IT strategy, g...	SP	L3	HR initiatives for IT	▲ Verzögert	0%	01.10.2025	30.06.2026	195	▲ Verzögert	Amelang Nicole (LIS)	Rollinger Alexander (LIS)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Manage HR4IT strategy, governane and framework Provide and develop IT workforce › Manage HR4IT strategy, g...	SP	L2	HR initiatives for IT	◦ Terminiert	0%	01.10.2025	31.12.2026	–	✓ Abgeschlossen	Amelang Nicole (LIS)	Rollinger Alexander (LIS)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–

PROZESS ▲	GRUPPE ⌵	EBENE ⌵	INITIATIVE ⌵	STATUS ⌵	% FERTIG ⌵	START ⌵	ENDE ⌵	DAUER (T) ⌵	ELABORATION ⌵	INITIATIVE LEAD ⌵	PROCESS MANAGER ⌵	CONSULTANT ⌵	FREIGABE ⌵	KOMMENTAR ⌵	
Manage IT compliance Manage IT risks and compliance › Manage IT compliance	MP	L2	Central area (Jan Müskens)	◀ In Arbeit	25%	01.10.2025	30.09.2026	261	◀ In Arbeit	Mueskens Jan (LHO)	Monnier Murielle (LEC)	Kreis Andreas (LLI)	–	–	
Manage IT costs Manage and control IT financials › Manage IT costs	MP	L2	IT planning and steering	◀ In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–	
Manage IT development programme Provide and develop IT workforce › Perform, learn and grow › ...	SP	L3	HR initiatives for IT	◦ Terminiert	0%	16.10.2025	16.10.2025	0	– Ohne Angabe	Grabmair Melanie (LIS)	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–	
Manage IT global orientation programme incl. job shadowing Provide and develop IT workforce › Perform, learn and grow › ...	SP	L3	HR initiatives for IT	▲ Verzögert	0%	15.01.2026	01.07.2026	120	▲ Verzögert	Grabmair Melanie (LIS)	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–	
Manage IT governance framework Manage IT governance framework	MP	L1	Corporate IT body	◀ In Arbeit	50%	07.01.2026	31.08.2026	169	◀ In Arbeit	Felder Max (LLI)	Mielenz Thomas (LMT)	Kunz Christina (LIS-MHP), Kreis Andreas (LLI)	–	–	
Manage IT knowledge Manage IT knowledge	SP	L1	ITSM	▲ Verzögert	100%	20.01.2026	30.06.2026	116	✓ Abgeschlossen	Kuerschner Philipp (LIS)	Sint Rachel (LBH)	Schroeder Michael (LIS)	19.03.2026	–	
Manage IT portfolio Manage IT portfolio	MP	L1	ITSM	◀ In Arbeit	78%	10.11.2025	15.05.2026	135	✓ Abgeschlossen	–	–	Frank Maren (LIS), Kunz Christina (LIS-MHP)	–	–	
Manage IT processes and continuous improvement Manage IT processes and continuous improvement	MP	L1	ITSM	◀ In Arbeit	21%	01.10.2025	31.05.2026	173	✓ Abgeschlossen	Rollinger Alexander (LIS)	Reiner Heiko (HAU-ITSA)	Hoermann Patrick (LLI)	–	–	
Manage IT project Manage IT project	SP	L1	IT project management	✓ Abgeschlossen	100%	14.07.2025	10.12.2025	108	✓ Abgeschlossen	Mühlbacher Christian (LIS)	Rollinger Alexander (LIS)	Frank Maren (LIS)	18.09.2025	–	
Manage IT project change request Manage IT project › Manage IT project change request	SP	L2	IT project management	✓ Abgeschlossen	100%	14.07.2025	10.12.2025	1	✓ Abgeschlossen	Mühlbacher Christian (LIS)	Rollinger Alexander (LIS)	Frank Maren (LIS)	18.09.2025	–	
Manage IT project portfolio Manage IT portfolio › Manage IT project portfolio	MP	L2	IT project management	▲ Verzögert	100%	10.11.2025	31.05.2026	145	✓ Abgeschlossen	Mühlbacher Christian (LIS)	Rollinger Alexander (LIS)	Frank Maren (LIS)	–	–	
Manage IT risks Manage IT risks and compliance › Manage IT risks	MP	L2	Central area (Jan Müskens)	◦ Terminiert	0%	01.10.2025	30.09.2026	261	– Ohne Angabe	–	Monnier Murielle (LEC)	–	–	–	
Manage IT risks and compliance Manage IT risks and compliance	MP	L1	n/a	◀ In Arbeit	22%	01.10.2025	30.09.2026	–	✓ Abgeschlossen	Mueskens Jan (LHO)	Monnier Murielle (LEC)	Hoermann Patrick (LLI)	–	–	
Manage IT service capacity Run IT service › Ensure IT service continuity › Manage IT servi...	CP	L3	ITSM	– Nicht geplant	0%	–	–	–	– Ohne Angabe	–	Sint Rachel (LBH)	Schroeder Michael (LIS), Boehme Matthias (LIS-BPMO)	–	–	

PROZESS ▲	GRUPPE ⌵	EBENE ⌵	INITIATIVE ⌵	STATUS ⌵	% FERTIG ⌵	START ⌵	ENDE ⌵	DAUER (T) ⌵	ELABORATION ⌵	INITIATIVE LEAD ⌵	PROCESS MANAGER ⌵	CONSULTANT ⌵	FREIGABE ⌵	KOMMENTAR ⌵
Manage IT service change Build IT Service › Manage IT service change	CP	L2	ITSM	✓ Abgeschlossen	100%	12.01.2026	30.06.2026	122	✓ Abgeschlossen	Sint Rachel (LBH)	Wiehe Alexander (COB)	Kunz Christina (LIS-MHP), Frank Maren (LIS)	15.04.2026	–
Manage IT service desk Run IT service › Provide IT service support › Manage IT servic...	CP	L3	ITSM	– Nicht geplant	0%	–	–	–	– Ohne Angabe	–	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	–
Manage IT service portfolio Manage IT portfolio › Manage IT service portfolio	MP	L2	ITSM	◀ In Arbeit	50%	01.04.2026	08.09.2026	115	◀ In Arbeit	Birgit Gerathewohl (LIS)	Reiner Heiko (HAU-ITSA)	Frank Maren (LIS), Kunz Christina (LIS-MHP)	–	–
Manage IT service provision request Deliver IT service › Manage IT service provision request	CP	L2	ITSM	▲ Verzögert	0%	01.04.2026	17.06.2026	56	▲ Verzögert	–	Schnurrenberger Christoph (LIS-LIN)	–	–	–
Manage IT service release Build IT Service › Manage IT service release	CP	L2	ITSM	◀ In Arbeit	50%	20.02.2026	30.06.2026	93	◀ In Arbeit	Hoeller Martin (LBH)	Wiehe Alexander (COB)	Kunz Christina (LIS-MHP), Frank Maren (LIS)	–	–
Manage IT skills Provide and develop IT workforce › Perform, learn and grow › ...	SP	L3	HR initiatives for IT	▲ Verzögert	0%	01.01.2026	30.06.2027	390	▲ Verzögert	Grabmair Melanie (LIS)	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Manage IT sourcing and procurement Manage IT sourcing and procurement	SP	L1	ITSM	◀ In Arbeit	25%	20.04.2026	08.07.2026	118	◀ In Arbeit	Dolderer Wolfgang (LIS)	Monnier Murielle (LEC)	Schoeberl Lorena (LBH)	–	–
Manage IT stakeholder relationships Manage IT stakeholder relationships	MP	L1	Corporate IT body	▲ Verzögert	0%	01.04.2026	23.12.2026	191	▲ Verzögert	Felder Max (LLI)	Mielenz Thomas (LMT)	Kreis Andreas (LLI)	–	–
Manage IT strategy Manage IT strategy	MP	L1	Corporate IT body	◀ In Arbeit	50%	02.02.2026	29.07.2026	128	◀ In Arbeit	Felder Max (LLI)	Mielenz Thomas (LMT)	Kreis Andreas (LLI)	06.05.2026	–
Manage IT talent pool and identify potential Provide and develop IT workforce › Perform, learn and grow › ...	SP	L3	HR initiatives for IT	◦ Terminiert	0%	16.10.2025	16.10.2025	0	– Ohne Angabe	Grabmair Melanie (LIS)	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Manage IT-C framework Manage IT risks and compliance › Manage IT compliance › Ma...	MP	L3	Central area (Jan Müskens)	◀ In Arbeit	25%	01.10.2025	30.09.2026	261	◀ In Arbeit	Mueskens Jan (LHO)	Monnier Murielle (LEC)	Kreis Andreas (LLI)	–	–
Manage IT-C strategy Manage IT risks and compliance › Manage IT compliance › Ma...	MP	L3	Central area (Jan Müskens)	◀ In Arbeit	25%	01.10.2025	30.09.2026	261	◀ In Arbeit	Mueskens Jan (LHO)	Monnier Murielle (LEC)	Kreis Andreas (LLI)	–	–
Mapping and evaluate IT career level Provide and develop IT workforce › Perform, learn and grow › ...	SP	L3	HR initiatives for IT	▲ Verzögert	0%	01.04.2026	01.01.2027	198	▲ Verzögert	Grabmair Melanie (LIS)	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Model and allocate IT costs Manage and control IT financials › Model and allocate IT costs	MP	L2	IT planning and steering	◀ In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–

PROZESS ▲	GRUPPE ⌵	EBENE ⌵	INITIATIVE ⌵	STATUS ⌵	% FERTIG ⌵	START ⌵	ENDE ⌵	DAUER (T) ⌵	ELABORATION ⌵	INITIATIVE LEAD ⌵	PROCESS MANAGER ⌵	CONSULTANT ⌵	FREIGABE ⌵	KOMMENTAR ⌵
Monitor and analyse events Run IT service › Monitor and report IT service performance › M...	CP	L3	ITSM	– Nicht geplant	0%	–	–	–	– Ohne Angabe	Kuerschner Philipp (LIS)	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	–
Monitor and report IT service financials Run IT service › Monitor and report IT service performance › M...	CP	L3	ITSM	– Nicht geplant	0%	–	–	–	– Ohne Angabe	Kuerschner Philipp (LIS)	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	–
Monitor and report IT service level Run IT service › Monitor and report IT service performance › M...	CP	L3	ITSM	◦ Terminiert	0%	15.04.2026	31.07.2026	0	– Ohne Angabe	Kuerschner Philipp (LIS)	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	Norbert Schwarz (MHP) wird für Philipp Kürschner den Prozess mit erarbeiten; Philipp ist weiterhin PO
Monitor and report IT service performance Run IT service › Monitor and report IT service performance	CP	L2	ITSM	◦ Terminiert	0%	15.04.2026	–	–	– Ohne Angabe	Kuerschner Philipp (LIS)	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	–
Monitor IT service risk and compliance Run IT service › Monitor and report IT service performance › M...	CP	L3	ITSM	– Nicht geplant	0%	–	–	–	– Ohne Angabe	Kuerschner Philipp (LIS)	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	–
Monitor to delegate Manage IT risks and compliance › Manage IT compliance › Mo...	MP	L3	Central area (Jan Müskens)	◀ In Arbeit	25%	01.10.2025	30.09.2026	261	◀ In Arbeit	Mueskens Jan (LHO)	Monnier Murielle (LEC)	–	–	–
Monitor user experience Run IT service › Monitor and report IT service performance › M...	CP	L3	ITSM	– Nicht geplant	0%	–	–	–	– Ohne Angabe	Kuerschner Philipp (LIS)	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	–
Onboard new IT employee and manager Provide and develop IT workforce › Perform onboarding › Onb...	SP	L3	HR initiatives for IT	◀ In Arbeit	50%	16.10.2025	30.04.2026	141	◀ In Arbeit	–	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Operate and maintain IT service Run IT service › Operate and maintain IT service	CP	L2	ITSM	▲ Verzögert	21%	15.10.2025	30.06.2026	185	▲ Verzögert	Kretz Lucas (COC-COT-IT)	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	–
Perform active sourcing Provide and develop IT workforce › Attract and hire employees ...	SP	L3	HR initiatives for IT	▲ Verzögert	0%	01.10.2025	31.12.2026	327	▲ Verzögert	Kiesewetter Ivana (LIS)	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Perform and measure process Manage IT processes and continuous improvement › Perform ...	MP	L3	ITSM	✓ Abgeschlossen	100%	01.10.2025	01.10.2025	1	✓ Abgeschlossen	Rollinger Alexander (LIS)	Reiner Heiko (HAU-ITSA)	Hoermann Patrick (LLI)	18.09.2025	–
Perform initial assessment of customer need Plan IT service › Perform initial assessment of customer need	CP	L2	Corporate IT body	▲ Verzögert	100%	01.08.2025	31.03.2026	3	✓ Abgeschlossen	Spieth Tina (LIS)	Mielenz Thomas (LMT)	Kunz Christina (LIS-MHP)	19.08.2025	–
Perform onboarding Provide and develop IT workforce › Perform onboarding	SP	L2	HR initiatives for IT	◀ In Arbeit	33%	16.10.2025	30.04.2026	141	◀ In Arbeit	–	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Perform operational process management Manage IT processes and continuous improvement › Perform ...	MP	L2	ITSM	◀ In Arbeit	25%	01.10.2025	31.05.2026	173	◀ In Arbeit	Rollinger Alexander (LIS)	Reiner Heiko (HAU-ITSA)	Rollinger Alexander (LIS)	18.09.2025	–

PROZESS ▲	GRUPPE ⌵	EBENE ⌵	INITIATIVE ⌵	STATUS ⌵	% FERTIG ⌵	START ⌵	ENDE ⌵	DAUER (T) ⌵	ELABORATION ⌵	INITIATIVE LEAD ⌵	PROCESS MANAGER ⌵	CONSULTANT ⌵	FREIGABE ⌵	KOMMENTAR ⌵
Perform SaaS Security Assessment Ensure Information security › Perform SaaS Security Assessment	SP	L2	Information security	◀ In Arbeit	50%	19.10.2025	30.11.2025	–	◀ In Arbeit	Hefele Michael (LIN-LIS)	Reiner Heiko (HAU-ITSA)	Hoermann Patrick (LLI), Rollinger Alexander (LIS)	–	–
Perform software selection Build IT Service › Design IT service › Perform software selection	CP	L3	Architecture management	▲ Verzögert	100%	01.10.2025	30.04.2026	152	✓ Abgeschlossen	Preiss Matthias (LBC)	Reiner Heiko (HAU-ITSA)	Hoermann Patrick (LLI)	14.10.2025	–
Perform vendor use case pitch and usability test Build IT Service › Design IT service › Perform software selectio...	CP	L4	Architecture management	✓ Abgeschlossen	100%	01.10.2025	30.04.2026	1	✓ Abgeschlossen	Preiss Matthias (LBC)	Reiner Heiko (HAU-ITSA)	Hoermann Patrick (LLI)	14.10.2025	–
Perform, learn and grow Provide and develop IT workforce › Perform, learn and grow	SP	L2	HR initiatives for IT	◀ In Arbeit	11%	01.10.2025	30.06.2027	456	– Ohne Angabe	Grabmair Melanie (LIS)	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Plan IT project Manage IT project › Plan IT project	SP	L2	IT project management	✓ Abgeschlossen	100%	14.07.2025	10.12.2025	1	✓ Abgeschlossen	Mühlbacher Christian (LIS)	Rollinger Alexander (LIS)	Frank Maren (LIS)	18.09.2025	–
Plan IT service Plan IT service	CP	L1	Corporate IT body	▲ Verzögert	100%	01.08.2025	30.04.2026	195	✓ Abgeschlossen	Spieth Tina (LIS)	Mielenz Thomas (LMT)	Kunz Christina (LIS-MHP)	–	–
Plan IT workforce Provide and develop IT workforce › Manage HR4IT strategy, g...	SP	L3	HR initiatives for IT	▲ Verzögert	0%	16.10.2025	31.12.2026	316	▲ Verzögert	Amelang Nicole (LIS)	Rollinger Alexander (LIS)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Plan process execution Manage IT processes and continuous improvement › Perform ...	MP	L3	ITSM	◀ In Arbeit	25%	12.01.2026	31.05.2026	100	◀ In Arbeit	Rollinger Alexander (LIS)	Reiner Heiko (HAU-ITSA)	Rollinger Alexander (LIS)	18.09.2025	–
Pre-board new IT employee and manager Provide and develop IT workforce › Perform onboarding › Pre-...	SP	L3	HR initiatives for IT	◀ In Arbeit	25%	16.10.2025	30.04.2026	141	◀ In Arbeit	–	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Provide and develop IT workforce Provide and develop IT workforce	SP	L1	HR initiatives for IT	◀ In Arbeit	15%	01.10.2025	30.06.2027	456	✓ Abgeschlossen	Amelang Nicole (LIS)	Rollinger Alexander (LIS)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Provide IT service support Run IT service › Provide IT service support	CP	L2	ITSM	▲ Verzögert	57%	16.10.2025	15.06.2026	173	▲ Verzögert	Kuerschner Philipp (LIS)	Sint Rachel (LBH)	Schroeder Michael (LIS)	–	–
Recommendation and EA approval Build IT Service › Design IT service › Perform software selectio...	CP	L4	Architecture management	✓ Abgeschlossen	100%	01.10.2025	30.04.2026	1	✓ Abgeschlossen	Preiss Matthias (LBC)	Reiner Heiko (HAU-ITSA)	Hoermann Patrick (LLI)	14.10.2025	–
Record and plan functional requirements Build IT Service › Design IT service › Perform software selectio...	CP	L4	Architecture management	✓ Abgeschlossen	100%	01.10.2025	30.04.2026	1	✓ Abgeschlossen	Preiss Matthias (LBC)	Reiner Heiko (HAU-ITSA)	Hoermann Patrick (LLI)	14.10.2025	–
Recruit employees and managers Provide and develop IT workforce › Attract and hire employees ...	SP	L3	HR initiatives for IT	▲ Verzögert	25%	01.10.2025	31.12.2026	327	◀ In Arbeit	Kiesewetter Ivana (LIS)	Mielenz Thomas (LMT)	Chen Leilei (LIS-BPMO), Hynek Tobias (LIS)	–	–
Report actual IT costs Manage and control IT financials › Manage IT costs › Report a...	MP	L3	IT planning and steering	◀ In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Moser Mario (LIS-LAH)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–

PROZESS ▲	GRUPPE ⌵	EBENE ⌵	INITIATIVE ⌵	STATUS ⌵	% FERTIG ⌵	START ⌵	ENDE ⌵	DAUER (T) ⌵	ELABORATION ⌵	INITIATIVE LEAD ⌵	PROCESS MANAGER ⌵	CONSULTANT ⌵	FREIGABE ⌵	KOMMENTAR ⌵
Requirements to measures Manage IT risks and compliance › Manage IT compliance › Re...	MP	L3	Central area (Jan Müskens)	◀ In Arbeit	25%	01.10.2025	30.09.2026	261	◀ In Arbeit	Mueskens Jan (LHO)	Monnier Murielle (LEC)	–	–	–
Review and maintain IT service continuity plan Run IT service › Ensure IT service continuity › Review and mai...	CP	L3	ITSM	– Nicht geplant	0%	–	–	–	– Ohne Angabe	–	Sint Rachel (LBH)	Schroeder Michael (LIS), Boehme Matthias (LIS-BPMO)	–	–
Review budget plan Manage and control IT financials › Create and maintain IT bud...	MP	L3	IT planning and steering	◀ In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Mielenz Thomas (LMT)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–
Revise and optimize budget plan Manage and control IT financials › Create and maintain IT bud...	MP	L3	IT planning and steering	◀ In Arbeit	50%	15.10.2025	–	–	– Ohne Angabe	Frank Nicole (LIS)	Mielenz Thomas (LMT)	Hynek Tobias (LIS), Kreis Andreas (LLI)	–	–
Run IT service Run IT service	CP	L1	ITSM	▲ Verzögert	17%	15.10.2025	25.09.2026	248	▲ Verzögert	Oey Kai (LIS)	Sint Rachel (LBH)	Schroeder Michael (LIS), Boehme Matthias (LIS-BPMO)	–	–
Steer and execute IT project Manage IT project › Steer and execute IT project	SP	L2	IT project management	✓ Abgeschlossen	100%	14.07.2025	10.12.2025	1	✓ Abgeschlossen	Mühlbacher Christian (LIS)	Rollinger Alexander (LIS)	Frank Maren (LIS)	18.09.2025	–
Strategic architecture process Manage enterprise architecture › Strategic architecture process	MP	L2	Corporate IT body	▲ Verzögert	0%	16.10.2025	30.04.2026	–	▲ Verzögert	–	–	–	–	–
Test and validate IT service Build IT Service › Test and validate IT service	CP	L2	ITSM	◀ In Arbeit	0%	04.05.2026	31.07.2026	–	◀ In Arbeit	Dalek Martin (LIS)	Wiehe Alexander (COB)	Kunz Christina (LIS-MHP)	–	–
Validate strategic fit Build IT Service › Design IT service › Perform software selectio...	CP	L4	Architecture management	✓ Abgeschlossen	100%	01.10.2025	30.04.2026	2	✓ Abgeschlossen	Preiss Matthias (LBC)	Reiner Heiko (HAU-ITSA)	Hoermann Patrick (LLI)	14.10.2025	–
Quelle: Process_Portfolio_Timeline.xlsx · data Draft-april26 Alle Kennzahlen, Diagramme und die Timeline reagieren auf dieselbe Filterauswahl. Build 2026-08-25 12:22 UTC														
